

Construction update

Ward: Mississauga Ward 1 – Councillor Dasko
Mississauga Ward 3 – Councillor Fonseca


Project name: 18-1310C – Dundas Street

Start date: November 2023

Expected completion: Summer 2025



Project map

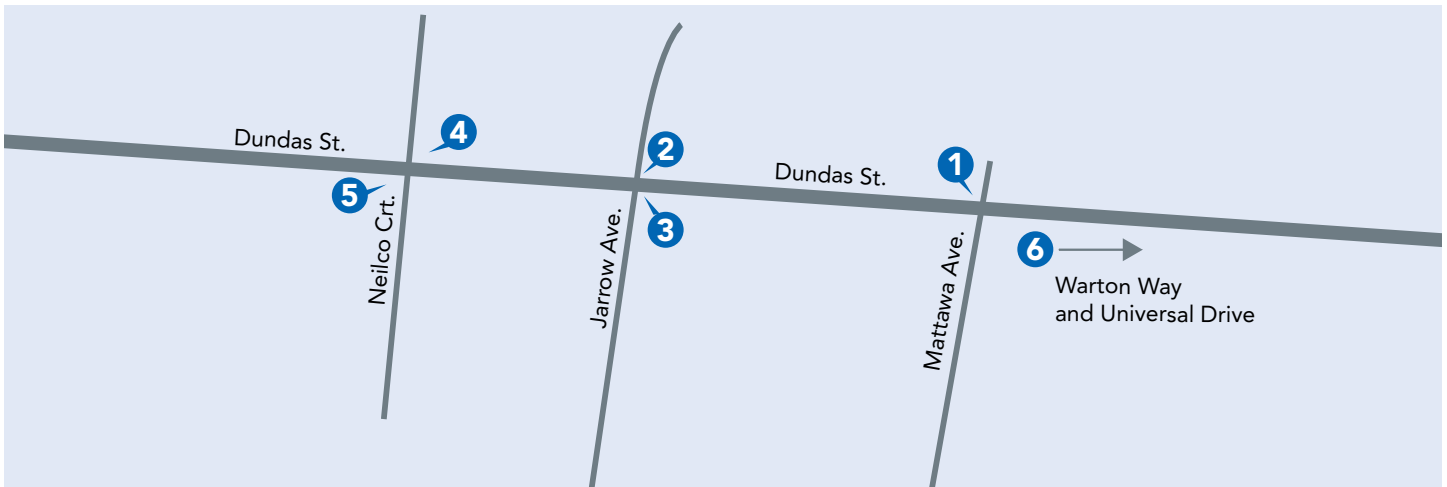

Mattawa Avenue intersection

Location 1



Traffic restrictions

- Intersection open in all directions
- Restricted lanes on west bound Dundas
- Dedicated left turn lane available into southside mall

Jarrow Avenue intersection

Location 2



Traffic restrictions

- Intersection open in all directions
- Restricted lanes on west bound Dundas
- Dedicated left turn lane available into southside mall

Location 3



Remaining work

- No active work next week – watermain installation across Dundas, east of Jarrow within next three weeks
- Final restoration mid 2025

Neilco Court intersection

Location 4



Traffic restrictions

- Intersection open in all directions
- Restricted lanes on west bound Dundas
- Dedicated left turn lane available into southside mall

Location 5



Remaining work

- Active construction
- Completing watermain installation
- Work including temporary road restoration completed within two weeks
- Final connection at Neilco and final restoration mid 2025

Wharton Way and Universal Drive intersection

Location 6



Traffic restrictions

- Restricted lanes on westbound Dundas
- Intersections open in all directions

Remaining work:

- Active construction
- Tapping watermain for future connection
- Work to be completed within one week including temporary road restoration
- Final restoration in mid 2025

WTR-0274 25/04
